



CITY OF HOT SPRINGS

Utilities Department

780 Adams Street

Hot Springs, Arkansas 71901

November 13, 2025

Sent via email

Leslie Allen-Daniel
Enforcement Analyst – Water Division
Arkansas Energy & Environment – Environmental Quality
5301 Northshore Drive
North Little Rock, AR 72118-5317

**RE: City of Hot Springs Utilities
Permit No. AR0033880 / AFIN 26-00145
Progress Report – Hot Springs Creek Pump Station**

Dear Ms. Allen-Daniel,

Hot Springs # 3 Sewer Lift Station and Hot Springs Creek Pump Station Improvements

Max Foote Construction Company, LLC, of Mandeville, Louisiana, has completed the upgrades and repairs to the Hot Springs #3 Sewer Lift Station. The contractor has mobilized to the Hot Springs Creek Pump Station and has begun demolition of existing equipment in preparation for new installations.

Improvements to the Hot Springs Creek Pump Station are scheduled for completion in February 2026. Max Foote and Eagle Electric of Benton, Arkansas, have been closely coordinating on the electrical requirements for the project to help streamline the construction process and maintain project efficiency.

System Performance

There was one sanitary sewer overflow (SSO) at Manhole 1866 in October.

Should you need further information, please contact me at (501)651-7730 or by email at mledbetter@cityhs.net.

Sincerely,

Monty Ledbetter
Utilities Director

Attachments: SSO Lab Results; CodeRed Notification; Environmental Cleanup Documentation

cc: Arkansas Energy & Environment | Richard Healey, Enforcement Manager
City of Hot Springs - Bill Burrough, City Manager; Denny McPhate, Deputy City Manager;
Harold Mauldin, Wastewater Facilities Operations Manager; Todd Piller, Capital Projects
Manager;
Consultants - Craig Johnson, Crist Engineers

October SSO REPORT for Manhole 1866 - Hot Springs Creek Basin

Manhole 1866 Sanitary Sewer Overflows – 362 Fontana Road

Overflow Date: 10/28/2025
End Date: 10/28/2025
Cause: Rainfall
Discharge: Approximately 36,000 Gallons discharged to Hot Springs Creek
Actions Taken: Environmental Cleanup, Disinfected, Deodorized, Raked/picked up and Spread Lime
CodeRed Issued: 10/28/2025
CodeRed Rescinded: 11/4/2025

Lab Results - Sample Sites are identical for all manholes

Sample Date:	10/28/2025	Sample Date:	10/31/2025	Sample Date:	11/3/2025
Site No.	E. coli (cfu)	Site No.	E. coli (cfu)	Site No.	E. coli (cfu)
1	>2419.6	2	42.5	2	5.2
		3	41.7	3	5.2
		4	29.2	4	4.1

Code Red and Notification Signs

Signage for October 28, 2025 SSO Event



Sign Site 1 Placed



Sign Site 1 Removed



Sign Site 2 Placed



Sign Site 2 Removed

ENVIRONMENTAL CLEANUP ACTIVITIES – Manhole 1866 – October 29, 2025



MH 1866 BeforeCleanup



MH 1866 BeforeCleanup



MH 1866 During Cleanup




MH 1866 During Cleanup

ENVIRONMENTAL CLEANUP ACTIVITIES – Manhole 1866 – October 29, 2025



MH 1866 After Cleanup

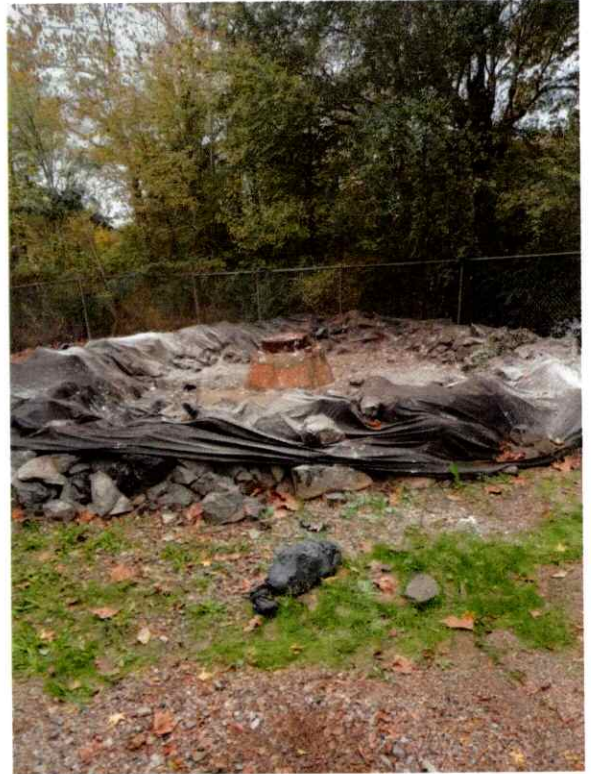

MH 1865 After Cleanup
